



ICT-INOV

MODERNIZING ICT EDUCATION FOR
HARVESTING INNOVATION

INTERNAL QUALITY ASSURANCE

INTERIM REPORT





Document Info	
Project reference	618768-EPP-1-2020-1-EL-EPPKA2-CBHE-JP
Deliverable / Task	T6.1
Dissemination level	Internal
Date	30.11.2022
Document version	1.0
Status	Final
Sharing	CC-BY-NC-ND
Authors	Carlos Vaz de Carvalho
Reviewer	Hariklia Tsalapatas
Contributors	All partners
Approved by	Steering Committee





CONTENTS

CONTENTS	3
INTRODUCTION.....	4
PROJECT SUMMARY	5
CONSORTIUM.....	5
WORK PLAN	6
QUALITY ASSURANCE METHODOLOGY	8
STRUCTURE, ROLES AND RESPONSIBILITES	8
DATA COLLECTION TOOLS	9
QUALITY ASSURANCE RESULTS.....	10
Meetings and events evaluation results.....	10
INTERNAL evaluation results	13
CRITERIA AND INDICATORS	15
DISCUSSION AND CONCLUSIONS	18





INTRODUCTION

The objective of a Quality Assurance process is to support the management entities in the production of concrete and high-quality results in line with the project objectives and work plan. To guide this process, a Quality Assurance Plan was designed in the beginning of the project, establishing a coherent set of guidelines, criteria and indicators by which all aspects of the project were to be measured and assessed.

This document presents the status of the Internal Quality Evaluation process at the time of the Interim Report and shows that the internal quality assurance plan has been followed closely and that the process generated valuable information to keep the project on track. The indicators clearly show a positive progress of the activities and the corresponding generation of high-quality products which reveals that the consortium was able to overcome all the initial issues created by the COVID pandemic.



PROJECT SUMMARY

Universities have the responsibility to modernize their educational practices to be able to develop highly skilled ICT professionals capable of innovating and putting ideas into action. This is crucial because it benefits individuals by building knowledge and skills for pursuing successful careers in a highly evolving sector therefore contributing to the community wellbeing through services that address industry and societal issues.

ICT-INOV aims to enrich ICT Higher Education in Asia, and specifically Malaysia, Vietnam, Nepal, and Pakistan, for promoting innovation by introducing a technology-enhanced, design thinking learning intervention for contributing to the development of an ICT workforce highly capable of innovation. The project mainly targets educators, students and Higher Education Institutions and the main results of the project are:

- A design thinking, experiential learning framework for innovation
- Physical labs and digital services for promoting collaboration in design thinking
- Educational activities that integrate design thinking
- Instructor training and community building towards the adoption of design thinking in ICT education

CONSORTIUM

ICT-INOV consortium gathers 12 Higher Education Institutions from Greece, Portugal, Estonia, Italy, Malaysia, Pakistan, Nepal, Viet Nam:

- PANEPISTIMIO THESSALIAS
- INSTITUTO POLITECNICO DO PORTO
- TALLINN UNIVERSITY
- EUROPEAN TRAINING AND RESEARCH ASSOCIATION
- UNIVERSITY OF MALAYA
- UNIVERSITI TENAGA NASIONAL SDN. BHD
- ISRA ISLAMIC FOUNDATION (GUARENTEE)LIMITED
- NATIONAL UNIVERSITY OF COMPUTER AND EMERGING SCIENCES NUCES

- TRIBHUVAN UNIVERSITY
- KATHMANDU UNIVERSITY
- TRUNG TAM XUAT SAC JOHN VON NEUMANN
- HANOI UNIVERSITY

WORK PLAN

The duration of the project is 36 months and is comprised of 7 Work Packages (3 technical WPs, 3 Management and Quality Assurance WPs and 1 WP for Dissemination and Exploitation).

WP1: Preparation (leader: Tallinn University)

- To analyse current practices in ICT education as well as learning needs per Partner Country and organization.

WP2: Methodological learning framework (leader: EU-Track)

- To develop an experiential learning framework for building innovation skills through design thinking and gamification.

WP3: Implementation (leader: University of Thessaly)

- To develop the physical and digital infrastructure for supporting design thinking in ICT education.

WP4: Capacity and community building activities (leader University of Malaya)

- To build a community of good practices on deploying design thinking for innovation

WP5: Dissemination and exploitation (leader: Universiti Tenaga Nasional)

- To disseminate widely and promote the adoption of project results
 - Developing a project portal

WP6: Quality Plan (leader: Porto Polytechnic)



- To establish the degree to which the project is implemented according to the goals set in this proposal

WP7: Project Management (leader: University of Thessaly)

- To ensure the smooth and timely implementation of the work plan





QUALITY ASSURANCE METHODOLOGY

The quality assurance methodology, defined in the QA plan, ensures the proper implementation of the activities and results of the project. It also ensures that all partners are fully involved in the different monitoring and evaluation mechanisms along the various project phases and report, on a periodic basis, about the activities they are leading and participating in.

STRUCTURE, ROLES AND RESPONSIBILITIES

The structure, roles and responsibilities in the QA process defined in the QA plan were the following:

The **Project Coordinator (PC)** is the responsible for the overall operation of the project and its smooth running, timeliness and accomplishment. He oversees financial and administrative management including the preparation of reports. The PC is the final responsible to ensure that all partners' contributions meet the expectations.

The **Steering Committee (SC)** supervises the implementation of the whole project. It is chaired by the PC and it is composed by one member of each partner. The SC is the arbitration body which implements the provisions of the Grant Agreement. In the SC meetings the members review interim results from the QA process and set interim (6-month) implementation goals. Evaluation results are to be made public at the end of the project implementation period in a corresponding report.

The **Quality Manager (QM)**, is responsible for the achievement of the quality objectives of the project. The duty of the QM is to monitor and evaluate the progress of the project and to ensure that all its activities are carried out properly according to the Quality Assurance plan and ensuring proper execution of the project to achieve its objective. The QM designed the monitoring and evaluation process and was responsible for selecting criteria, indicators, and data collection tools.

The **External Evaluator (EE)**, monitors and evaluates the progress of the project with an external perspective and is responsible for producing the deliverables 6.2 and 6.3.





The **Work Package Leader (WPL)** - Each WPL is responsible for the detailed co-ordination and reporting of the specific WP. If needed, meetings of the partners involved in the Output are to be organized and chaired by the WPL. For each deliverable, within the WP, the WPL will assign direct responsibility either to himself/herself or to an associate individual. The WPL is the person that is contacted by the PC as part of the monitoring of progress towards completion of the deliverables.

The **Partners** are involved in the QA process by reporting and assessing the project progress and the produced deliverables.

DATA COLLECTION TOOLS

The project quality is assured through the monitoring and evaluation of the quality of two main aspects: the project processes and the project deliverables.

In each project meeting (including online meetings) a specific session was dedicated to Quality Assurance to analyse the internal and external evidences and other monitoring data. Furthermore, after each meeting, a section of the meeting evaluation questionnaire was dedicated to the assessment of the current state of the partnership and the project progress.

The quality of the key project processes was also monitored and assessed through an internal self-evaluation of the consortium by the project partners. This evaluation was done by each partner through a questionnaire with an assessment of the performance of the consortium and of the current state of the project activities. For this interim report, the internal evaluation was performed together with the evaluation of the third SC meeting.

Event evaluation was done by all participants through a relevant questionnaire that follows the template annexed to the QA plan.

All these tools were complemented by the observation of ongoing processes like communication, the analysis of the produced documentation (like meeting minutes, reports from events and training) and also the assessment of the produced deliverables.




QUALITY ASSURANCE RESULTS

During the first part of the project, data was collected in the two first SC meetings conducted online and the two first training events. An internal evaluation survey was conducted in parallel with the 3rd SC meeting (the event itself was evaluated but the results will only be considered for the second half of the project). The results were presented to the SC and partners through specific reports available in the WP6 area in the common project folder. The summary of each evaluation is provided next.

MEETINGS AND EVENTS EVALUATION RESULTS


Kick-Off Meeting Evaluation Report (Online, 24th - 26th February 2021)

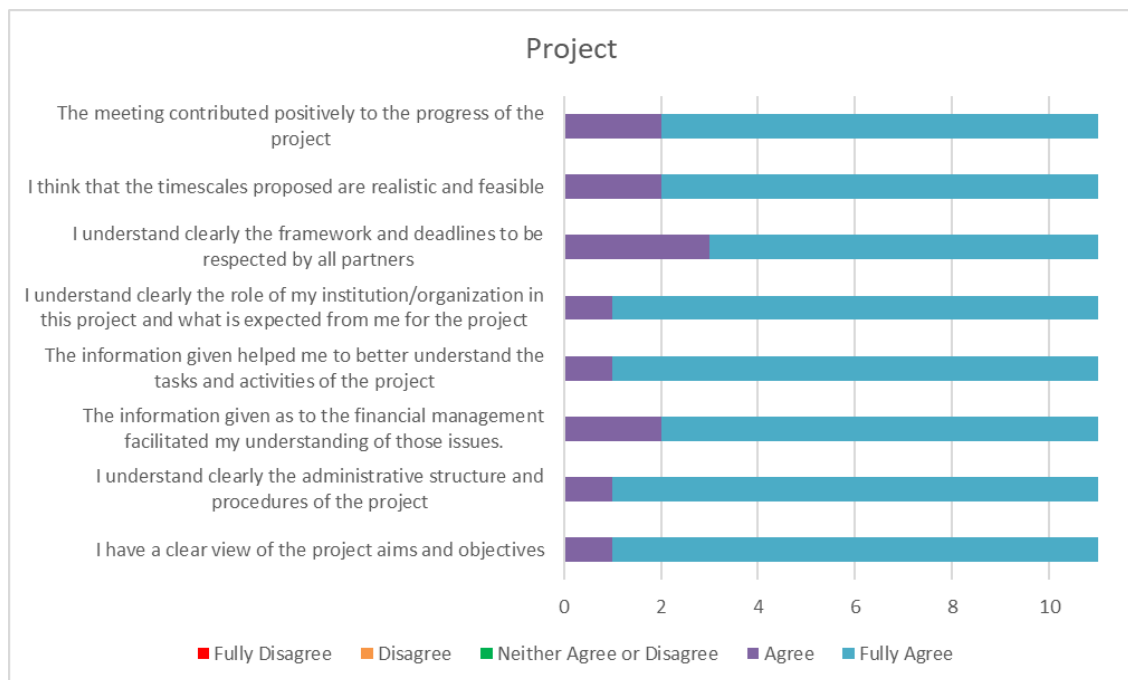

The overall evaluation indicated that the reaction to the meeting was positive and that it served to better explain the individual responsibilities and tasks each partner owns, as well as to complete a first “get to know” of the partners and integrate all the parts of the consortium. The partners had a positive assessment of the future of the project, and showed some common expectations for the outcomes and share the uncertain concern of the projects dissemination and implementation plan caused by the extraordinary

pandemic situation. All the questions were evaluated with a very high satisfaction level, around 85%.

2nd Meeting Evaluation Report (Online, 1-3 November, 2021)



The overall assessment of the 2nd project meeting was very positive and partners felt satisfied with the way it helped them clarify previous doubts and better understand the project’s goals, objectives and deadlines. The great majority of the participants gave very good feedback, agreeing or fully agreeing with the statements presented, and not expressing any major difficulty or concern for the near future. Overall, partners were happy with the consortium organisation and collaboration, they recognised the importance and relevance of ICT-INOV’s tools and activities, and they felt they had a lot to benefit from transnational cooperation and the further integration of the project deliverables in their schools and institutions.

However, this meeting had a slightly less positive evaluation than the previous one, and some doubts and uncertainties that had not been expressed in the kick-off meeting, were now communicated by the participants. From the analysis of the first sections of the questionnaire, it is possible to conclude that not all partners felt like they fully


understand the role of their organisations in the partnership, they claimed that the project’s aims and objectives are not very clear, and still manifest some doubts regarding the administrative procedures. This was later confirmed in the open section, where some partners claimed that they still have doubts about the effectiveness of the project’s methodology, about the usage of the project’s tools, and where they also showed some concerns regarding the timetable and the completion of all project’s deliverables. One aspect that was mentioned both in the closed questions and in the open section is that the online tool used for the meeting was not favourable to the communication (in fact, it seemed to affect it negatively), which is something that the coordinator and the partners of the project definitely need to pay attention to, in order to ensure a better flow of communication in the future and to guarantee a productive and collaborative meeting.

1st Instructor Training Evaluation Report (Porto Portugal, 31 January – 4 February, 2022)



The general conclusion of the event evaluation is that it was very positive and successful and that partners felt satisfied with the usability of what they learned and its relevance for their professional careers. There were minor issues related to the platform used but that did not prevent the participants from getting the most from the training. Finally there were some suggestions regarding the integration of gamification contents and reduce the length of the training. All the assessment topics were evaluated with a satisfaction level over 85%.

2nd Instructor Training Evaluation Report (Hanoi Vietnam, 27 June – 1 July, 2022)



The general conclusion of the evaluation of the second instructor training was that it was very positive (although slightly less positive than the previous one) and successful and that partners felt satisfied with course and its relevance for their professional careers. The organization in small multicultural groups was highly praised and the level of interaction and involvement of facilitators and participants was also considered very positive. All in all, the training structure, organization, contents and approach seems to have reached a very high plateau of quality. For the next event it will be necessary to assess if the suggestions relating to new contents (gamification) and activities should be followed. All the assessment topics were evaluated with a satisfaction level over 85%.


All the meetings and events were considered positive and approved as the percentage of satisfaction was higher than 3 in more than 70% of the answers.

INTERNAL EVALUATION RESULTS

The internal evaluation survey covered aspects related to leadership, coordination, collaboration, partner involvement, etc. Participants were asked to score from 1 (very negative) to 5 (very positive).

All the answers were clearly positive with an overwhelming number of “Very Positive” scores. The most positive aspects related to the competence and commitment displayed by the coordinator, the quality of the project impact, the quality of the project

monitoring and evaluation processes and tools and the commitment and involvement of the partners.

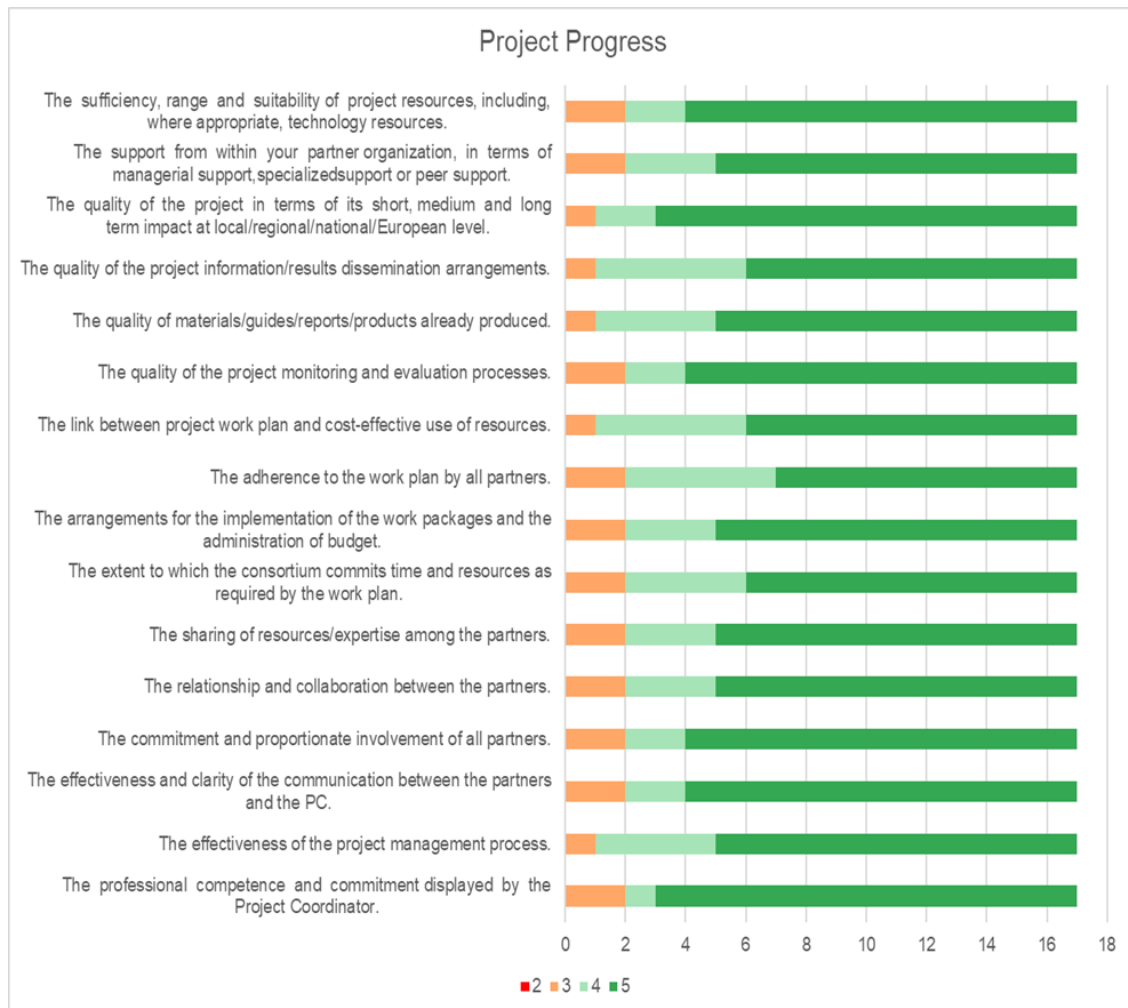



CRITERIA AND INDICATORS

The constant observation of the project progress, the produced reports and the analysis of the deliverables allows to quantitatively measure the current status of the project.

	Criteria	Indicators	Quantified objectives (min.)	Status
WP1	Depth of the research performed (strategies, policies, projects, etc.)	1.1 Number of sources used in desk research	1.1: 100	1.1: 103
		1.2 Number of external cases (strategies, policies, projects, etc.) used in the research	1.2: 30	1.2: 64
		1.3 Number of institutional cases identified and used in the research	1.3: 12	1.3: 32
WP2	Depth of the research performed	2.1 Number of sources used in desk research	2.1: 50	2.1: 52
		2.2 Number of external cases (strategies, policies, projects, etc.) used in the research	2.2: 10	2.2: 12
	Assessment of students' needs	2.3 Number of students involved	2.3: 360	2.3: 368
		2.4 Number of HEI involved	2.4: 15	2.4: 16
	Depth and scope of the educational framework	2.5 Number of identified needs supported by the framework	2.5: 15	2.5: 16
		2.6 Proposed design thinking and gamification features	2.6: 6	2.6: 12
Depth and scope of the institutional strategy	2.7 Number of consortium HEI implementing the institutional strategy	2.7: 12	2.7: 12	
	2.8 Number of external HEI reached to develop an institutional strategy based on ICT INOV educational framework	2.8: 10	2.8: 24	
WP3	Physical laboratories	3.1. Number of laboratories installed	3.1: 8	3.1: 8
		3.2. Number of users of the laboratories	3.2: 1200	3.2: 400
	Digital learning service	3.3. Number of students involved	3.3: 750	3.3: 2113
		3.4. Number of educators involved	3.4: 160	3.4: 71
	Digital content repository	3.5 Number of educational resources/activities integrated	3.5: 50	3.5: 63
		3.6 Number of users of the repository	3.6: 500	3.6: 620





	National events	3.7 Number of events 3.8 Number of participants	3.7: 6 3.8: 150	3.7: 17 3.8: 164
	Webinar organization	4.1 Number of events 4.2 Number of participants	4.1: 6 4.2: 150	4.1: 2 4.2: 56
WP4	National events	4.3 Number of events 4.4 Number of participants	4.3: 6 4.4: 150	4.3: 4.4:
	Final conference	4.5 Number of participants 4.6 Average perceived satisfaction of the participants	4.5: 100 4.6: 75%	4.5: 4.6:
	Training events	4.7 Number of participants 4.8 Average perceived satisfaction of the participants	4.7: 30 4.8: 75%	4.7: 48 4.8: 85%
WP5	Dissemination tools produced and released	5.1 Number of unique visitors to the project website 5.2 Number of likes/followers in social media 5.3 Number of publicity materials printed (flyers, etc.) and distributed 5.4 Number of organizations/stakeholders receiving the e-newsletters	5.1: 10 000 5.2: 2.000 5.3: 2500 (1st edition) + 2500 (2nd edition) 5.4: 500	5.1: 7.320 5.2: 2.150 5.3: 375 5.4: 267
	Exposure in external events, publications or in the media	5.5 Number of posters and/or technical/scientific papers published in conferences/workshops 5.6 Number of articles published in technical/scientific journals 5.7 Number of articles in the media/press referring to the project	5.5: 6 5.6: 3 5.7: 6	5.5: 4 5.6: 5.7: 23
	Extent of the project dissemination efforts	5.8 Number of dissemination activities carried out 5.9 Number of individuals reached	5.8: 150 5.9: 50.000	5.8: 162 5.9: 41.500
	Range of external organizations reached	5.10 Number of external organizations contacted 5.11 Number of external organizations engaged (or that expressed interest) in project activities	5.10: 150 5.11: 25	5.10: 35 5.11: 11





WP6	Quality of the Monitoring and Evaluation Plan	6.1 Ratio of instruments proposed/applied for indicators of realization 6.2 Ratio of instruments proposed/applied for indicators of result	6.1: 90% 6.2: 90%	6.1: 100% 6.2: 100%
	Evidences of the Monitoring and Evaluation process	6.3 Number of quality indicators below threshold 6.4 Number of end-users involved in evaluation activities	6.3: 4 (max) 6.4: 200	6.3: 0 6.4: 68
WP7	Compliance in the implementation of the planned tasks and in the releasing of project deliverables	7.1 % of tasks completed on time 7.2 % of deliverables released on time	7.1: 70% 7.2: 80%	7.1: 75% 7.2: 90%
	Value of the communication and workflow process among partners	7.3 Number of partners not attending meetings (maximum) 7.4 Number of e-mail messages between partners	7.3: 2 (max) 7.4: 150	7.3: 1 7.4: 377
	Degree of effective use of resources	7.5 % of financial execution in the first year 7.6 % of operational actual costs overrun (staff, travel and subsistence, subcontracts, other) compared to project budgeted values	7.5: 40% 7.6: 10%	7.5: 7.6:



DISCUSSION AND CONCLUSIONS

The different tools and activities established to monitor and ensure the quality of the project have been adequate for the goal. Through them it was possible to collect a significant amount of data to provide feedback on the progress of the project and, with it, to suggest to the Steering Committee how to cope with obstacles. That was the case of the COVID pandemic that created a significant disruption in the beginning of the project. At that moment, the QA process together with the management process were fundamental to ensure the smooth continuation of activities.

The QA procedures and tools have been well accepted and understood by the partners (4,65 out of 5) and their involvement in the different QA activities is well above 80%. The number of expected participants in evaluation activities (indicator 6.4) almost reached the planned threshold for the entire project which shows this commitment.

In terms of the overall project progress and deliverables, all the data collection tools show highly positive results. Meetings and events have been scored always above the 80% threshold. The quantitative indicators show a well-advanced project and all the finished work packages are entirely green. The values in yellow show indicators that have not reached the threshold yet but as they correspond to tasks that will continue in the second half of the project they are not troublesome. The only activities that the SC needs to promote further are the following:

- The number of users in the created labs (the COVID pandemic delayed the establishment of the labs and some of them were only in full force very close to the middle of the project therefore it is expected that the number of users in the second half will grow way beyond the established threshold)
- The number of educators using the platform (the platform was launched in the second year, according to the plan, and its use has been growing so it is expectable that the number of educators using it will also grow steadily)
- The national events, either for training or promotional purposes
- The webinars with an international scope

- The publication of results in international technical/scientific journals



Co-funded by the
Erasmus+ Programme
of the European Union

This project is funded with support from the European Commission. This publication reflects the views only of the author, and the Commission cannot be held responsible for any use which may be made of the information contained therein.
